
[m<sup>3</sup>/day]

## Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings

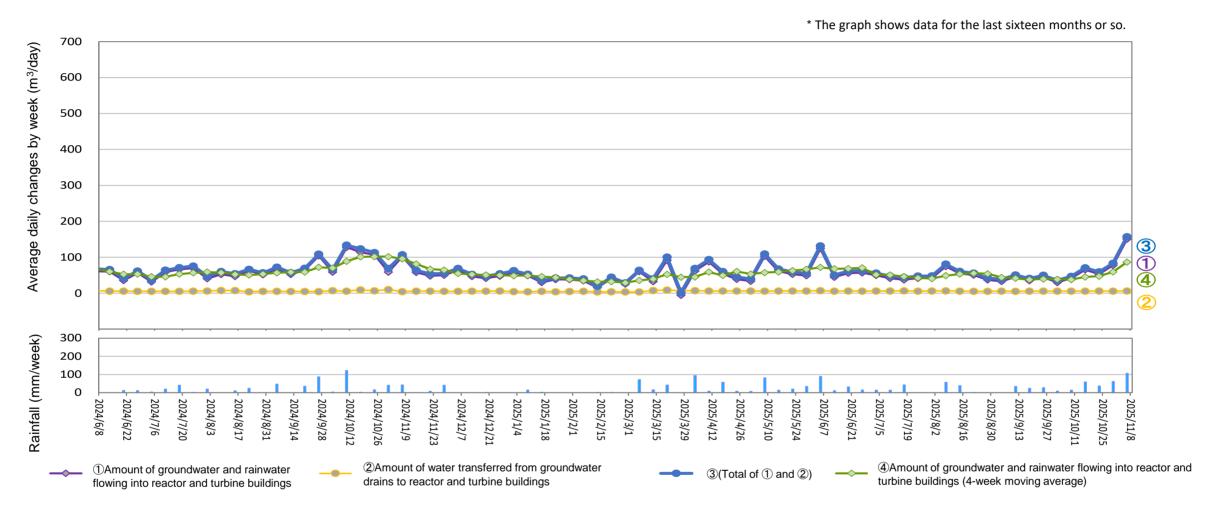

Amount of water transferred from groundwater drains to reactor and turbine buildings (From October 30, 2025 to November 5, 2025)

Date	Temporary storage tanks				
	Α	В	С	Total (α)	
From October 30 to November 5	0	0	0	0	

(Re	(Reference)			
Between Units 1-2	Between Units 2-3	Between Units 3-4	Total (β)	Amount of water transferred to turbine buildings $[(\alpha)+(\beta)]$
6	0	0	6	6

①Amount of groundwater and rainwater flowing into reactor and turbine buildings: 151 m³/day, ②Amount of water transferred from groundwater drains to reactor and turbine buildings: 6 m³/day, ③(Total of ① and ②): 157 m³/day, Rainfall: 106.0 mm/week

There may be a difference between the sum of the individual data and the total value since the total value is the sum of the data with the first decimal place.

<sup>\*</sup> Figures for ①, ③ and ④ have been calculated after elaborating some of cross sectional area of the process main building since April 4, 2024. Nevertheless, figures may be estimated to be a negative value since the calculation still contains uncertainty.

(Reference) ④ Amount of groundwater and rainwater flowing into reactor and turbine buildings (4-week moving average): 87 m³/day

(Reference) Changes in the amount of water transferred from groundwater drains to reactor and turbine buildings and in the amount of groundwater and rainwater flowing into the buildings from the start of measurement

